

Book # 62 - Dr. #8

OFFICE OF COUNTY ENGINEER
RAMSEY CO. MINN.

Lake Imp. Survey


ROUND LAKE PIPE LINE


From..... To.....

Road Acc't. No.

Date Filed.....

File.....

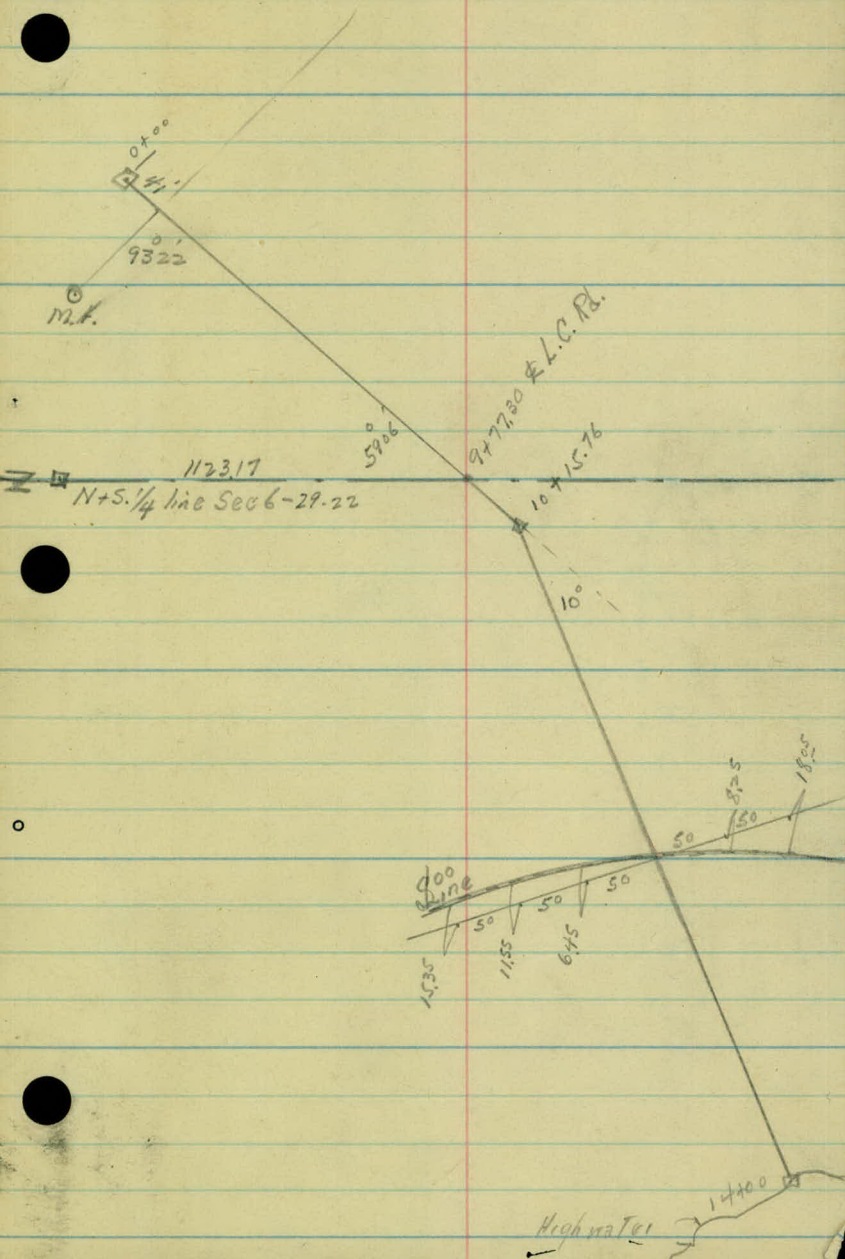

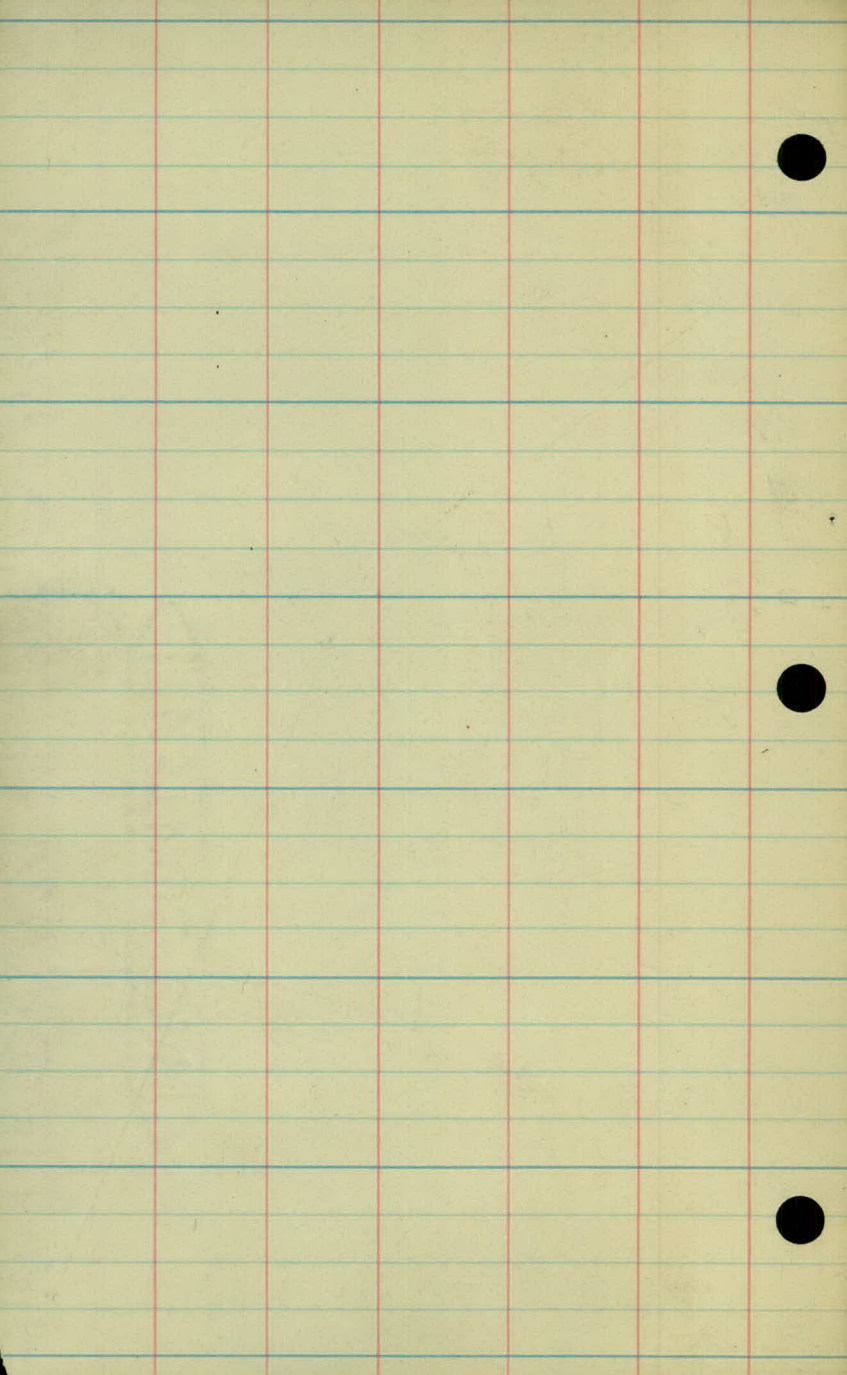

Round Lake Survey

6-29-33

14+00

End Proj.

12+75²³ $\neq$ Line

10+15⁷⁶ Δ Pt.

10°00' Rt.

9+77³⁰ = $\neq$ of Little Canada Rd +

0+00

App. $\neq$ M. V. P. W.

6-29-33

Weber
Wilke
Stienmann

2" x 2" Hub.

P.R. 4.72 2" x 2" Hub.

cor. C.C.M.
Found.

699
L2

3846

15" R.E.
45" W.

8" W.H.
52.78

2" x 2" Hub.

80.40 6" T.M. C.W.

B.M.	4.49	928.55		924.06
B.M.	1.63	925.05	5.13	923.42
T.P.	0.12	912.08	13.09	911.96
T.P.	0.10	899.19	12.99	899.09
T.P.	3.92	892.85	10.26	888.93
B.M.			6.24	886.61
0+00			13.4	79.5
0+91			12.2	80.7
1+00			9.9	83.0
1+08			7.7	85.2
1+14			10.0	82.8
+50			6.8	86.1
+63			8.1	84.7
+72			6.5	86.4
✓			3.7	89.2
+50			3.7	89.2
+92			4.3	88.6
3			6.3	86.6
+10			5.9	87.0
+14			3.8	89.1
T.P.	10.29	899.22	3.92	888.93
4			8.6	91.6
5			6.0	93.2
T.P.	13.09	912.17	0.14	899.08
+71			10.8	901.4
6			8.9	903.3
+50			4.6	907.6

spt in P.P. opposite white Bungalow N. side Round Lt.

spt in P.P.

Lt Δ pt 10+15.76

Nail in 12" Oak 3' Lt Sta 1+05.

Ground Elev. approx Ctr W. Wks. R/W.

Cut.

Cut.

912.17

7		2.6	909.6
	13.39 925.35	0.21	911.96
8		8.5	916.9
+38		5.2	920.2
9		4.3	921.1
+36		3.8	921.6
+77	± L.C.Ld.	3.0	922.4
+93		3.2	922.2
10		3.9	921.5
+15	Δ Pt.	3.6	921.8
B.M.	6.19 929.61	1.93	923.42
11		6.4	923.2
12		5.7	923.9
+27		4.2	254 R/w line
+45		4.8	924.8
+56		5.8	Toe Fill 923.8
+7523	± R.L.	2.7	926.9
+86		4.2	925.4
13		8.0	Toe of Fill 921.6
+10		7.3	922.3
+24		10.4	R/w line 919.2
B.M.	0.16 921.18	8.59	921.02
+55		11.6	909.6
TP	0.27 908.54	12.91	908.27
14		5.3	903.2
		11.85	896.69

Cut

Cut.

Spk in T.P. Lt 13 + 20

End Proj. approx. High water mark.
Water Sur. as of 6-29-33.

