

BK. 31 Dr. 12 BK. 31 Dr. 12

OFFICE OF COUNTY ENGINEER
RAMSEY CO. MINN.

Fence.....Survey

Mitchell Prop......

From Yadnais Blvd......

Road Acc't. No.

Date Filed 8-3-48..... File


Report on Fence Condition
along Verdais Blvd. at
Mitchel Prop.

INDEX.	Page
South Fence	1-11
North "	12-16


11-4-47

1130 am Rec
11/4/47

Completed
11/15/47

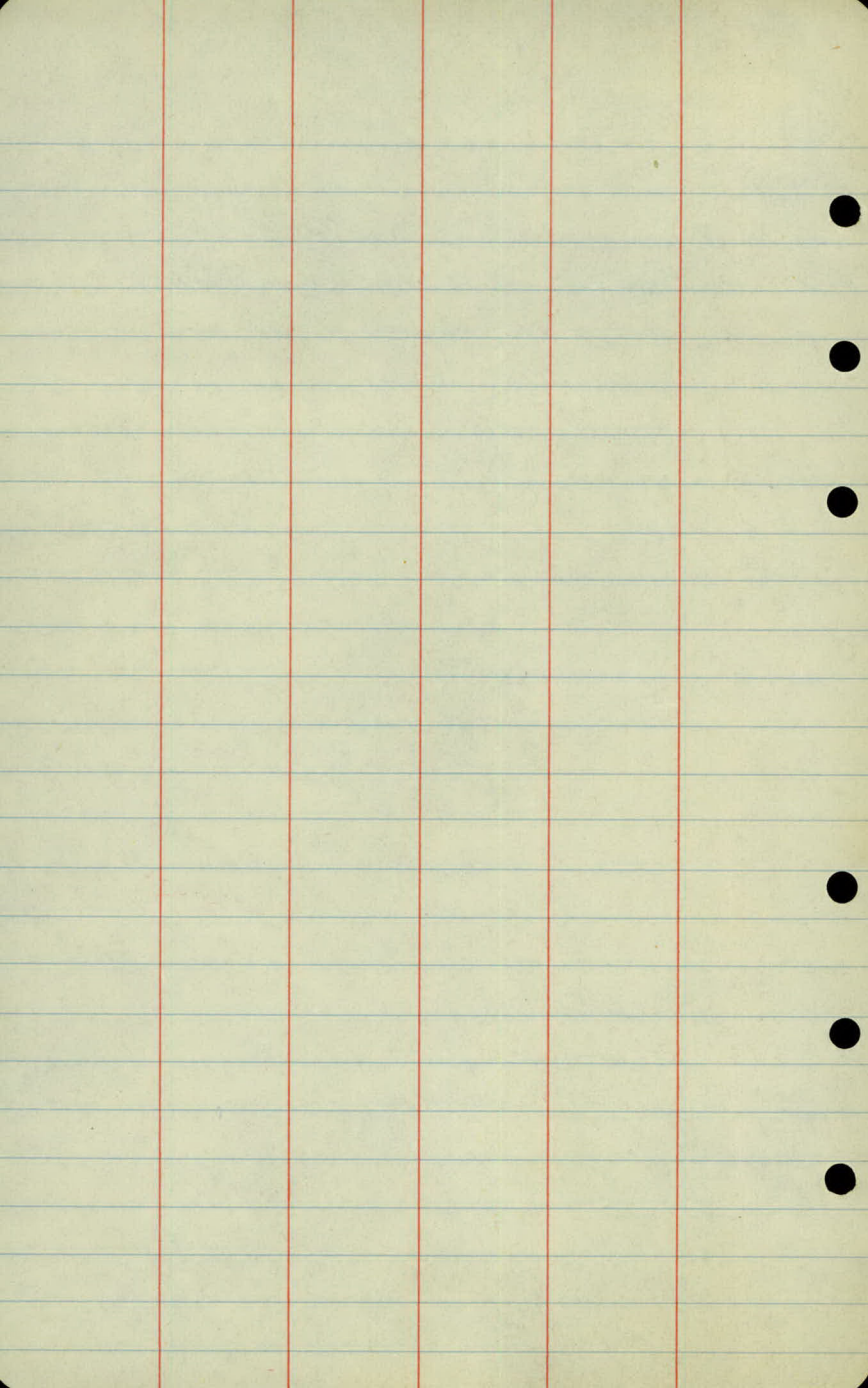

Fence Design

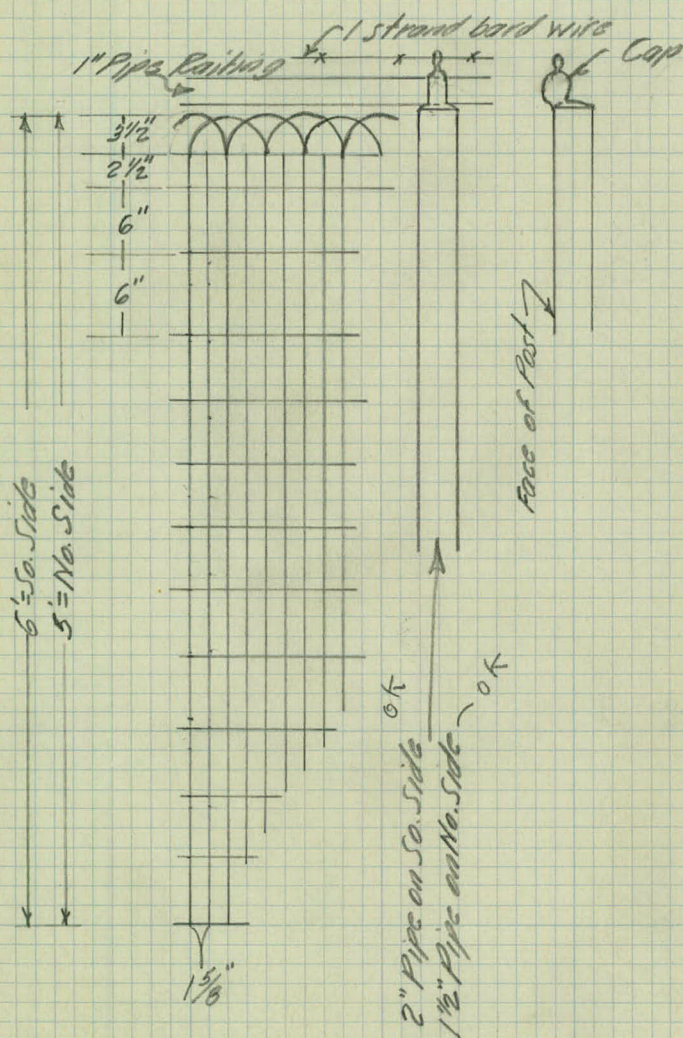

(OVER)

$1\frac{1}{2}"$

? North fence has $\frac{1}{2}"$ pipes and end posts
and gate posts are $4"$ pipes.

? South fence has $1\frac{1}{2}"$ pipes and end
posts are $2"$ pipes

1
Fence on south side of road

Sta

0 +00 = East Fence Post OK

+08 Iron Post - Replace

+14.8 Post Loosening - Straighten

↙ Fence Warped & Bent - Replace
+21.6 Post - OK

+28.4 Post OK

+36.7 Post - Replace

+41.8 Post - Replace

+52.4 Post - Replace

K.P.
A.M.
M.B.

2

0413 0413

} Top Rail Bent - Replace

0421

sta.

0 +60.6 Post-Replace

+68.7 Post-ok.

+76.7 Post-ok.

+84.5 Post-ok.

+92.8 Post-Replace

1 +01 Post-Replace

+09.7 Post-ok.

+17.6 Post-ok.

Sta.

1 +25.7 Post-ok.

+33.2 Post-ok.

+40.7 Post-ok.

+48.8 Post-ok.

+56.8 Post-Replace

+64.5 Post-ok. is loose replace concrete

+70.3 Top Rail broke at coupling - Weld -

+72.9 Post-ok.

+80.6 Post-ok.

2 sq. ft fence bent - straighten

Sta.

1 +88.6 Post-ok

+96.6 Post-ok.

2 +104.8 Post ok

+112.5 Post ok.

+120.5 Post ok.

+128.3 Post ok.

+136.3 East Gate Post ok.

Bottom & center cross pipe on gate
are gone - Replace

+141 West Gate Post ok Plum to fit gate

24

10.1.1911 1.1.1911

10.1.1911 1.1.1911

10.1.1911 1.1.1911

10.1.1911 1.1.1911

10.1.1911 1.1.1911

10.1.1911 1.1.1911

10.1.1911 1.1.1911

Sta.

Replace wire fence

+50.5 East Gate Post ok.

+63 West Gate Post ok.

+71.6 Post ok.

+76.4 Post ok. - is loose - replace conc.

+86.7 Post Replace

+91.6 Post ok. - is loose - replace conc.

3 +02.6 Post ok.

+10.9 Post ok. - is loose - Replace conc.

1912

1912 Jan 1 - 1912 Jan 2

1912 Jan 3 - 1912 Jan 4

1912 Jan 5 - 1912 Jan 6

1912 Jan 7 - 1912 Jan 8

1912 Jan 9 - 1912 Jan 10

1912 Jan 11 - 1912 Jan 12

1912 Jan 13 - 1912 Jan 14

1912 Jan 15 - 1912 Jan 16

Sta.

3 +18.7 Post ok. - is loose - Replace conc.

+26.2 Post ok. - is loose - Replace conc. - Paint

+33.6 Post ok. same as +26.2

+42 Post ok. same as +26.2

+49.8 Post ok. - is loose - Replace conc.

+58 Post ok. - is loose - Replace conc.

+66.2 Post. - Replace.

+74.4 Post ok.

+13 } Top Rail Bent - Replace
+19 }

+22 } Replace with new fence
+53 }

Sta.

3 +82 Post ok - is loose - Replace conc.

+90.4 Post ok.

+98.4 Post - Replace

4 +66.7 Post ok - is loose - Replace conc.

+14.3 Post - same as +66.7

+22.4 Post - same as +66.7

+30.6 Post - same as +66.7

+38.5 Post - same as +66.7

191 } Top Rail Bent - Replace
198 }

Sta.

A +46.8 Post - same as +46.7

+54.1 Post - same as +46.7

+61.8 Post - same as +46.7

+70.1 Post - same as +46.7

+77.4 Post - same as +46.7

+85.6 Post - same as +46.7

+93.1 Post - same as +46.7

B +01.1 Post - same as +46.7

+54.1 to end of fence replace top barb wire.

sta.

5 +08.6 Post - Replace

+16. Post ok place conc.

+23.8 Post - same as +16

+31.7 Post - same as +16 Weld cap to post -

+39.5 Post - same as +16

+48.8 Post - same as +16

+56.6 Post & conc. ok. - is loose in swamp -

+64.4 Post - same as +56.6


+38 to end replace with new fence

weld cap to post

sta

5 +72.7 Post-ok. Weld cap to post

+81.3 End post-ok - Plum

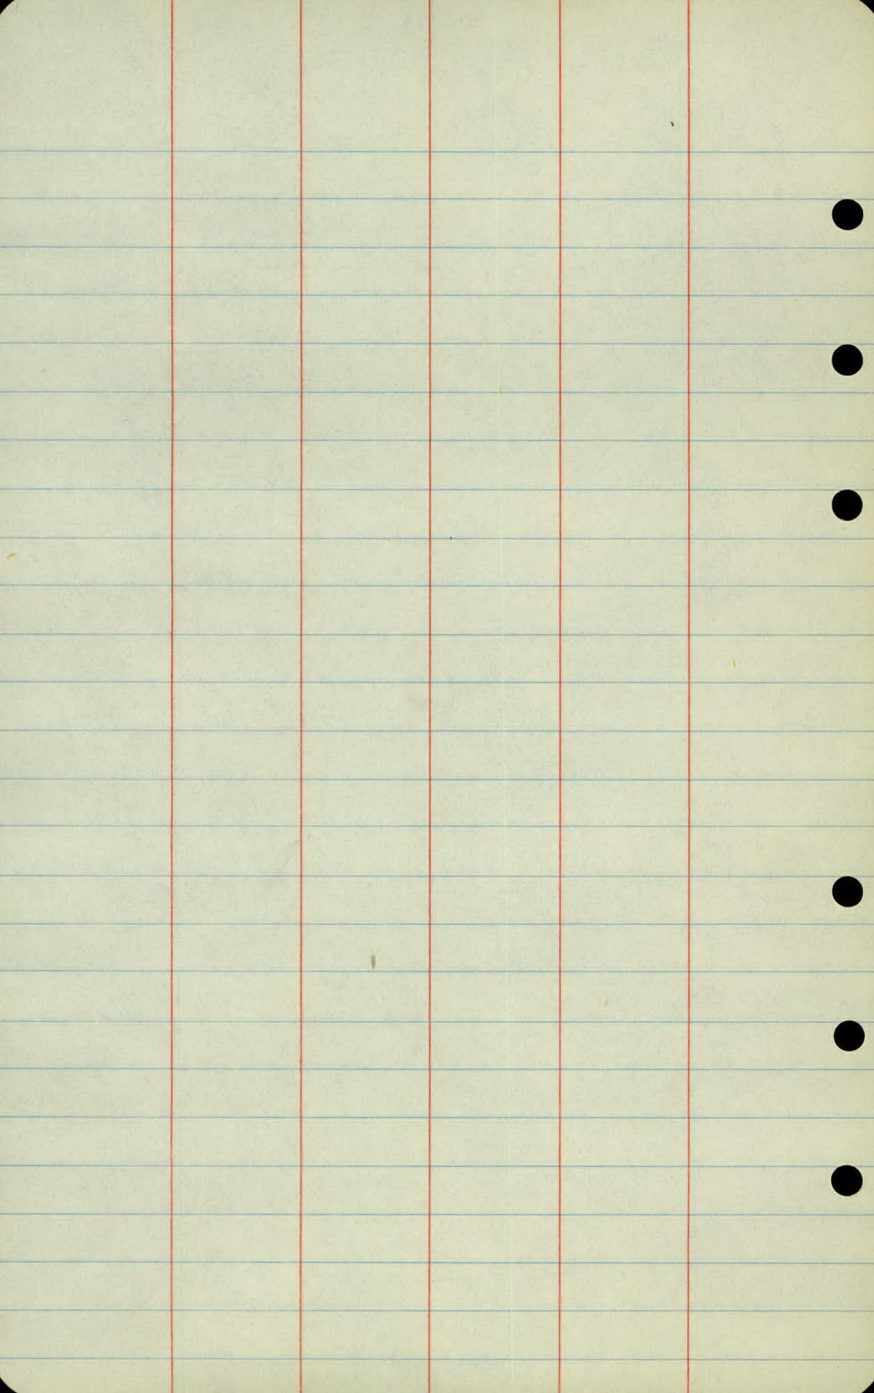

Fence on North side of Road.

Sta

0 +00 East Fence Post ok.

+07.9 Post ok

+16 Post ok

+23.8 Post ok

+31.8 Post ok.

+39.7 Post - Replace

+47.6 Post ok.

+55.4 Post - Replace

Sta

0 +63.1 Post ok.

↙ Replace Fence
+71.2 Post ok.

+79.2 Post ok.

+86.9 Post ok.

+94.8 Post. Replace post - Remove stump
↙ Fence loose - Tighten

1 +03. Post ok.

+10.8 Post ok.

+18.9 Post ok.

+21.5 Repair fence at stump.

Sta.

1 +27 Post ok

+34.7 Post ok.

+42.8 Post ok

+50.5 Post ok

+58.5 Post ok.

+66.4 Post ok.

+74.5 Post ok.

2 +42.7 Post - Replace

+49.5 Fence bent around rotted stump.
Remove stump.

+70- stump - same as +49.5

Sta.

2 +50.6 Post-Replace

3 +22 Post-Replace

4 +17 End Fence Post
